Project Planning Phase
Project Planning (Product Backlog, Sprint Planning, Stories, Story points)

Date	16 August 2026
Project Name	Employee Raise Issue – Record Producer & Service Portal Integration
Maximum Marks	5 Marks

Here is the polished and professionally rewritten version of your **Product Backlog, Sprint Schedule, Project Tracker, and Velocity Analysis**.

The language has been upgraded to align with formal Agile Scrum and enterprise project delivery methodologies, including standard user story syntax (*"So that I can..."*) and refined metric terminology.

Product Backlog & Sprint Schedule

Sprint Assignment	Epic / Functional Domain	User Story ID	Agile User Story / Technical Task	Story Points	Priority	Resource Assignment

Sprint-1	Discovery & Solution Architecture	**US-01**	**As an** employee, **I want to** report workplace-related incidents via a centralized intake form, **So that** I no longer rely on fragmented email or informal communication channels.	2	High	Individual

Sprint-1	Discovery & Solution Architecture	**US-02**	**As a** platform stakeholder, **I want** the data dictionary, custom fields, choice lists, and dependencies clearly mapped, **So that** the implementation remains structurally sound and consistent.	1	High	Individual
Sprint-1	Discovery & Solution Architecture	**US-03**	**As an** employee, **I want** a simplified, intuitive, and guided form layout, **So that** I can easily provide accurate issue details without friction.	2	High	Individual

Sprint-2	Schema & Core Configuration	**US-04**	**As a** ServiceNow administrator, **I want** to provision the custom Employee Issue table (`u_employee_issue`) with appropriate data types, **So that** submitted data is reliably stored as structured database records.	3	High	Individual

Sprint-2	Schema & Core Configuration	**US-05**	**As an** employee, **I want** to select a specific Category and Subcategory classification, **So that** my issue can be precisely categorized and routed for resolution.	2	High	Individual
Sprint-3	Intake Portal & Engine Delivery	**US-06**	**As an** employee, **I want** to access the Employee Raise Issue Record Producer directly within the Service Portal Catalog, **So that** I can submit tickets via a user-centric web interface.	3	High	Individual

Sprint-3	Intake Portal & Engine Delivery	**US-07**	**As a** ServiceNow administrator, **I want** the Record Producer catalog variables to map seamlessly to their target custom table fields, **So that** portal inputs accurately generate a backend transactional record.	2	High	Individual

Sprint-3	Intake Portal & Engine Delivery	**US-08**	**As a** ServiceNow administrator, **I want** to implement automated field validations and a Category-Subcategory dependency matrix, **So that** incomplete or invalid data is rejected prior to database commit.	2	High	Individual

Sprint-4	Quality Assurance & Handover	**US-09**	**As a** QA tester, **I want** to execute end-to-end functional testing covering portal submission, data mapping, and validation rules, **So that** I can verify system integrity against defined requirements.	2	High	Individual

Sprint-4	Quality Assurance & Handover	**US-10**	**As a** project owner, **I want** the solution's configuration blueprints and test execution records thoroughly documented, **So that** the system can be formally reviewed and transitioned to operations.	1	Medium	Individual

Project Tracker & Execution Metrics


Sprint ID	Planned Capacity (Story Points)	Sprint Duration	Target Start Date	Target End Date	Actual Story Points Completed	Actual Release Date
Sprint-1	5	3 Days	03 Aug 2026	05 Aug 2026	5	05 Aug 2026
Sprint-2	5	3 Days	06 Aug 2026	08 Aug 2026	5	08 Aug 2026
Sprint-3	7	3 Days	10 Aug 2026	12 Aug 2026	7	12 Aug 2026

Sprint-4	3	3 Days	13 Aug 2026	15 Aug 2026	3	15 Aug 2026
Total	**20**	**12 Days**	—	—	**20**	**Project Closed**

Velocity Performance Analysis

Velocity serves as a core diagnostic metric to calculate the project team's output capacity over explicit developmental cycles. For this individual delivery track, the project realized a **100% completion rate**, delivering **20 story points** across four distinct 3-day sprints.

- $AverageSprintVelocity = \frac{TotalStoryPointsCompleted}{TotalCompletedSprints} = \frac{20}{4} = 5.0 StoryPoints/Sprint$
- $AverageDailyVelocity = \frac{TotalStoryPointsCompleted}{AggregateProjectDuration(Days)} = \frac{20}{12} \approx 1.67 StoryPoints/Day$

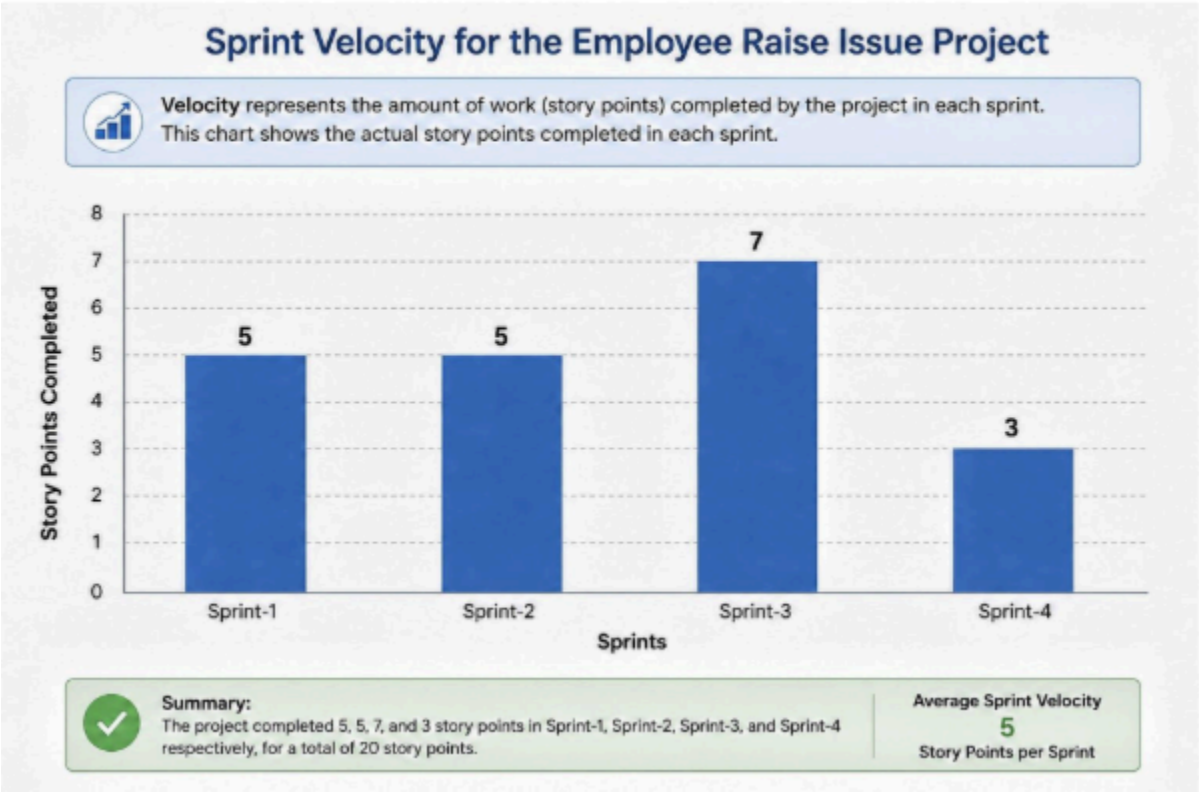

Burndown Chart:

A Burndown Chart represents the amount of work remaining against the planned project timeline. For this project, the chart tracks the remaining

story points across the four planned sprints.
The project begins with 20 story points. As stories are completed during each sprint, the remaining work decreases until all 20 story points are
completed at the end of Sprint-4.

